

RescueSwarm: An Indigenously Sourced Autonomous Multi-UAV System for Post-Disaster Search, Localisation and Payload Delivery

Research and Development Funding Proposal

Swastik Kumar

Department of Electronics & Communication Engineering

Thapar Institute of Engineering & Technology

Patiala, Punjab, India

skumar6_be24@thapar.edu

Abstract—India recorded 5.4 million internal displacements from disasters in 2024, the highest figure in twelve years, and the binding constraint on survivor outcomes is the speed with which casualties are located and reached. Ground and boat-based search is slow and hazardous; helicopter search is fast but scarce and expensive. This proposal describes RescueSwarm, a three-aircraft autonomous unmanned aerial system that surveys a designated area, detects and geolocates survivors, and delivers a standardised relief kit to each, under a single operator and without any reliance on cellular or internet infrastructure. The system is designed around a deliberate constraint: indigenous sourcing wherever the budget permits it, both because supply-chain sovereignty is a national priority and because domestic lead times are roughly half those of imports, which directly buys flight-test days inside a schedule-limited programme. The configuration costed here reaches approximately 45 % Indian content, and I state which lines were deferred to reach the requested figure and what restoring them would cost. I present the system architecture, the sizing and error models that fix its design point, the simulation evidence obtained to date, a market-verified cost basis, and a phased work plan. I am explicit throughout about which figures are measured, which are modelled, and which remain assumed; no aircraft has yet flown, and the proposal is structured so that a reviewer can distinguish demonstrated capability from projected capability without reading the source material. The requested funding is INR 9.94 L over an eight-month build.

Index Terms—unmanned aerial systems, multi-robot coordination, search and rescue, coverage path planning, RTK geolocation, edge inference, indigenous manufacturing, disaster response

I. INTRODUCTION AND PROBLEM STATEMENT

A. The operational gap

India records among the highest disaster-displacement figures in the world. The Internal Displacement Monitoring Centre reports **5.4 million internal displacements in India during 2024** — the highest in twelve years — of which 2.4 million were triggered by a single monsoon flood season in Assam [8]. The scale of the response problem is therefore not in question; what is in question is how quickly the people displaced by it can be found.

Post-flood search and rescue in India is dominated by a single quantity: the elapsed time between the onset of the

event and the moment a survivor is both *located* and *reached*. Nationally deployed capability addresses the second of these far better than the first. Boat teams and ground parties can reach a survivor once told where to go, but they search slowly, at high risk to the crew, and with poor coverage of debris fields and rooftops. Rotary-wing aircraft search quickly but are scarce, costly per flight hour, and are typically committed to evacuation rather than to systematic area survey.

The consequence is that *localisation* is the bottleneck. A search asset that can systematically cover an assigned polygon, detect human figures in cluttered post-flood imagery, and report each detection as a coordinate accurate to a few metres would materially change the tasking of every downstream resource.

B. Why a swarm rather than a single aircraft

A single multirotor with a useful payload and a fifteen-minute endurance covers a disappointing area. Coverage scales with the number of simultaneously operating aircraft, but so does operator workload, and a system requiring one pilot per aircraft does not deploy well in a disaster. The engineering problem is therefore not simply flight, but *coordinated autonomous flight under a single operator*: area decomposition, task allocation, deconfliction, consolidated reporting, and graceful degradation when the command link is lost.

C. Why indigenous sourcing is a design constraint, not a slogan

I treat domestic sourcing as a first-class design constraint for two reasons, only one of which is political.

The first is sovereignty: a disaster-response asset whose critical components have a single foreign supplier is a strategic liability, and national policy correctly prioritises domestic capability.

The second is schedule, and in a programme of this length it dominates. My supplier survey puts typical import lead times at four to six weeks against two to three weeks domestically. In a programme whose binding constraint is an eight-week flight-test window, that difference is not a procurement detail

— it is the difference between two test campaigns and one. Indigenisation, in this programme, buys flying days.

D. Contributions of the proposed work

- 1) A three-aircraft autonomous survey-and-delivery system operable by a single operator with no network dependency, sized and costed against market-verified Indian components.
- 2) A geolocation error budget that treats survivor coordinate accuracy as the primary system output, and an architecture that meets it using a team-owned RTK base rather than any external correction service.
- 3) A coordination scheme — static equal-area decomposition with boustrophedon coverage and greedy claim-and-lock task allocation — selected for determinism and verifiability over optimality.
- 4) An evidence discipline in which every published number regenerates from its model in continuous integration, and in which measured, modelled and assumed quantities are separated by construction.

II. OBJECTIVES AND SCOPE

A. Primary objectives

- O1** Survey a designated area autonomously with three cooperating aircraft under one operator and one ground control station.
- O2** Detect human figures in nadir imagery at a ground sample distance sufficient for reliable classification, with onboard inference and multi-frame temporal fusion.
- O3** Report each detection as a geodetic coordinate with a circular error probable within a few metres.
- O4** Deliver a standardised relief kit to each confirmed survivor location by controlled free-fall release.
- O5** Operate with no cellular, internet or cloud dependency at any point in the mission.
- O6** Maximise value-weighted indigenous content across the priced bill of materials without compromising O1–O5.

B. Explicit non-objectives

I state these because proposals of this kind are frequently over-scoped, and because each exclusion is a deliberate engineering decision rather than an omission.

- **Not a casualty-evacuation platform.** The payload class is a relief kit, not a person, and no growth path to the latter is claimed.
- **Not beyond-visual-line-of-sight certified.** The design operates within a bounded geofence; regulatory expansion is future work.
- **Not a night or all-weather system.** The perception stack is visible-band. Thermal imaging is identified as the highest-value future extension but is outside this programme.
- **Not a survivor-triage system.** The system reports position and delivers a kit; it makes no medical assessment.

III. RELATED WORK AND STATE OF THE ART

A. Coverage path planning

Area decomposition for multi-robot coverage is mature. Divide Areas for Optimal Multi-Robot Coverage (DARP) produces equal-area, connected, robot-specific regions and is the natural reference method [1]. Classical boustrophedon decomposition [2] remains the standard in-region motion primitive for sensor footprints that are rectangular in the body frame.

I adopt a static equal-area partition with boustrophedon in-region coverage rather than a full DARP implementation. This is a deliberate trade of optimality for determinism: a static partition produces an identical, inspectable plan for identical inputs, which is a precondition for the verification regime described in Section V-A. DARP is retained as design rationale and as a future-work path where dynamic reallocation becomes necessary.

B. Multi-robot task allocation

The Consensus-Based Bundle Algorithm (CBBA) is the canonical decentralised auction method for multi-agent assignment [3]. Its guarantees depend on a consensus phase over a communication graph. For a three-aircraft system with a reliable star topology to a single ground station, I implement greedy claim-and-lock with a deterministic tie-break, which is materially simpler to verify and whose worst-case behaviour on three agents is well within acceptable bounds.

C. Aerial detection of people

Small-object detection from altitude is the governing difficulty: a supine adult at survey altitude occupies a few tens of pixels. Slicing-aided hyper inference (SAHI) and related tiling strategies substantially improve small-object recall by running detection on overlapping crops rather than a downsampled full frame [4]. Purpose-built aerial person datasets such as SARD [5] and the broader VisDrone benchmark [6] provide the transfer-learning base; neither contains post-flood Indian terrain, which is why a field data campaign is a funded line in this programme rather than an assumption.

D. Airborne payload delivery

The dominant error term in airborne delivery is release state — velocity and wind — rather than release altitude. Mathisen *et al.* demonstrate autonomous ballistic airdrop from a small fixed-wing UAV and report a mean delivery error of 5.5 m, with the release state computed dynamically against wind and vehicle velocity and re-optimised in flight precisely because that term dominates [7]. This is the decisive argument for a multirotor in this role: a rotorcraft can null its groundspeed to near zero before release and thereby remove the dominant error term outright, which a fixed-wing cannot. The delivery budget in Section IV-F exploits exactly this.

TABLE I
AIR VEHICLE DESIGN POINT (PER AIRCRAFT)

Parameter	Value
Configuration	Quadrotor
Rotor diameter	18 in
Maximum take-off mass	6.36 kg
Fleet mass (3 aircraft)	19.08 kg
Regulatory fleet cap	25 kg
Battery	6S3P Li-ion 21700, 292 Wh
Cells per aircraft	18
Static thrust-to-weight	2.0
Hover endurance	15.3 min
Design mission duration	7.7 min
Survey altitude	60 m AGL
Ground sample distance	≤ 2.0 cm/px
Survey groundspeed	8 m/s
Payload	4 kits $\times$ 200 g
Geofence radius	600 m

E. Positioning

Real-time kinematic correction from a locally surveyed base is standard practice and is the only route to sub-metre relative positioning without an external network [10]. Since the system may not use internet or cellular services, a team-owned base station is not merely preferable but required.

IV. PROPOSED SYSTEM ARCHITECTURE

A. Design point

Table I states the aircraft design point. Every value is produced by a sizing model held in the repository and regenerated in continuous integration; none is transcribed by hand.

The thrust-to-weight ratio of 2.0 and the hover endurance of 15.3 minutes against a 7.7-minute design mission are both reserve policies rather than performance targets: the mission is sized to be completed comfortably within half the available energy, because the failure mode that ends a competition or a deployment is an aircraft that does not return.

Fig. 1 gives the mass statement behind those figures. Two features drive the rest of the design. Structure and battery together are 46 % of maximum take-off mass, which is why airframe mass fraction and pack chemistry are the two sensitivities carried in the risk register rather than, say, avionics choice. The survivor kits are 800 g — 12.6 % of MTOW and fixed by the mission at four kits of exactly 200 g — so payload is an input to the sizing loop, not an output of it. This is why propulsion and energy resist cost reduction in Section VII in a way that avionics does not: they are sized by a payload that is not negotiable, so cheaper parts of the same class are available but a smaller aircraft is not.

B. Segment architecture

The system comprises three segments, shown in Fig. 2.

1) *Air segment*: Three identical quadrotors, each carrying a Pixhawk-standard autopilot running ArduPilot [9], a dual-band NavIC/GNSS receiver providing RTK position, a nadir-mounted 12MP camera, an edge inference module, a four-

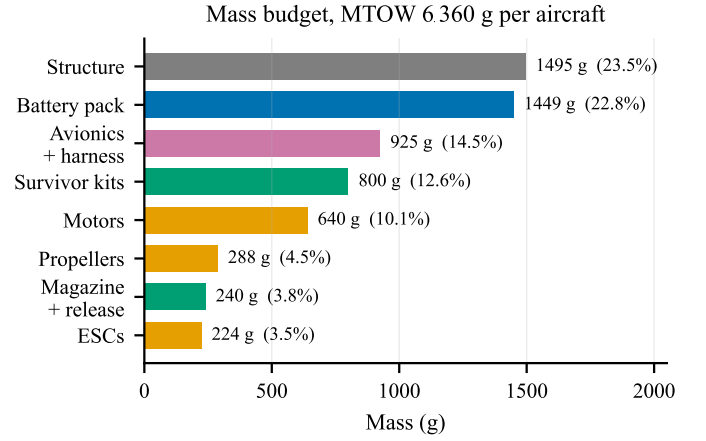


Fig. 1. Mass budget per aircraft. Generated from docs/sizing/model-output.txt. The fleet figure of 19081 g carries 4919 g of growth allowance against a 24 kg internal target — 26 % build overweight tolerated — inside the 25 kg regulatory cap.

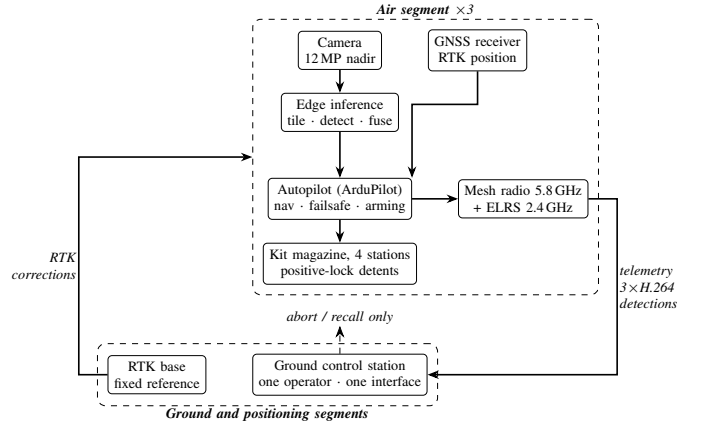


Fig. 2. System architecture. The only permitted downlink commands are abort and recall; the ground station is architecturally incapable of originating a retask, waypoint change or drop command. Detection runs onboard, so the downlink serves the operator rather than the algorithm.

station kit magazine with positive-lock detents, a 5.8GHz mesh radio for telemetry and video, and a 2.4GHz ExpressLRS link carrying safety-pilot control and abort independently of the autonomy stack.

2) *Ground segment*: A single ground control station presenting one unified operator interface. The station is architecturally incapable of originating a retask, waypoint change or drop command; abort and recall are the only permitted downlink commands, and are implemented as an explicit exception. This is a structural safety property rather than a policy: the relevant code paths are absent from the deployed build, not merely guarded.

3) *Positioning segment*: A team-owned RTK base station, positioned and set to a fixed reference from its first three-dimensional fix within the setup window. Launch is gated on a three-dimensional fix rather than an RTK fix; the first geotag is gated on RTK-fixed, and detections made before convergence are geotagged in float and re-fused once fixed. This decoupling

TABLE II
GEOLOCATION ERROR BY CONFIGURATION

Case	Configuration	RSS error
A	No RTK, single-frame	3.09 m
B	RTK, single-frame	~1.3 m
C	RTK + multi-frame fusion + calibrated ground plane	0.91 m

recovers approximately ninety seconds of setup time that a survey-in procedure would otherwise consume.

C. Geolocation error budget

Survivor coordinate accuracy is the primary system output, and the error budget is therefore the governing analysis of the whole design. Total error is the root sum of squares of GNSS position error, boresight and lever-arm residual, attitude error, terrain-model error and timing skew.

Table II shows the dominant conclusion: positioning quality, not optics, governs. This is what makes RTK a scoring requirement rather than an optimisation, and it is why the RTK receiver and its base station survive every cost-reduction pass in Section VII while a great deal else does not. The *second* receiver, which supplies moving-baseline heading, is a different case and is deferred to a measurement — see Section VII.

Multi-frame fusion is effectively free. At 60 m altitude and 8 m/s groundspeed, forward overlap yields on the order of fourteen independent observations of each target per pass even at a conservative 2 Hz inference rate. Those observations are used both for temporal confirmation, which suppresses false positives, and for geolocation averaging.

Fig. 3 shows both effects quantitatively. Panel (a) makes the positioning argument unarguable: losing the RTK fix moves the error by nearly an order of magnitude, and a 3-D-only fix at 3.67 m RSS consumes most of the 5 m delivery allowance before ballistics or position-hold error are counted. Panel (b) shows why fusion is worth having but not worth over-investing in — it divides the random terms by $\sqrt{n}$ and leaves boresight and target extent untouched, so the curve departs from the ideal $1/\sqrt{n}$ line and flattens by about five frames. Twenty frames is not twice as good as five, and the roughly fourteen frames the geometry supplies for free sit comfortably past the knee.

D. Perception and inference budget

A 12 MP sensor at 60 m yields a ground sample distance of approximately 2 cm/px, at which a supine adult subtends roughly fifty pixels — small, but within reach of tiled inference. Running detection on the full-resolution frame would require 48 tiles per frame and is far beyond the thermal and compute envelope of any module in this mass class. A two-times downsample with 20 % tile overlap requires 12 tiles per frame; at a 2 Hz inference rate this is 24 inferences per second at 640×640 , which is within the demonstrated throughput of the 26-TOPS-class accelerator selected in Section VII.

This is the single most benchmark-sensitive figure in the design. Published throughput for comparable models on comparable hardware spans roughly 24 to 41 frames per second, and the lower end of that range leaves no margin. Hardware benchmarking before design freeze is accordingly a funded, scheduled activity rather than an assumption.

E. Communications

Regulatory rules require the ground station to display a live camera feed from *each* aircraft. Three independent MJPEG streams would demand 4.5–6 Mbps against a link budget of approximately 2.5 Mbps. The system therefore uses H.264 encoding served through a media gateway, carrying three concurrent WebRTC streams in approximately 2.7 Mbps, with per-feed rate reduction under congestion rather than feed switching. Detection runs onboard; the downlink serves the operator, not the algorithm.

Band diversity is provided without a third radio. The 5.8 GHz mesh carries video, telemetry and coordination; a 2.4 GHz ExpressLRS link carries safety-pilot control and abort, and is independent of the autonomy stack. Both operate in delicensed bands and both comfortably cover the 600 m geofence. A further link in the 865–867 MHz short-range-device band would add a third independent path and is the correct extension when funding allows; it is deferred rather than fitted, and Section VII-E records the reasoning.

F. Payload delivery

Kits are released at 6 m above ground level, gated on a residual groundspeed below 0.3 m/s. At that release state, ballistic dispersion contributes approximately 0.32 m to total delivery error; combined with geolocation and position-hold error the root-sum-square is approximately 1.5 m with RTK active. Release altitude is chosen low enough that wind drift remains under a metre in realistic conditions, and high enough for safe clearance above a person and above debris.

Positive-lock mechanical detents on each station ensure that a power interruption cannot release a kit. This is treated as a safety-critical item and is excluded from cost reduction by policy.

G. Mission sequence

Fig. 4 shows the autonomous mission sequence. Two properties are worth drawing out. First, the launch stagger lives in the mission file as an explicit delay before each take-off command, not in operator timing — this is what converts a 1.31 m closest approach into the 64.80 m of Fig. 5. Second, every terminal branch converges on return-to-launch: link loss, low battery and operator abort share one recovery path rather than three.

V. METHODOLOGY AND WORK PLAN

The programme is organised into ten phases. Phases P1–P5 are analysis, procurement and integration; P6–P10 are progressively more demanding flight test. The eight-week flight-test window spanned by P6–P10 is the binding schedule

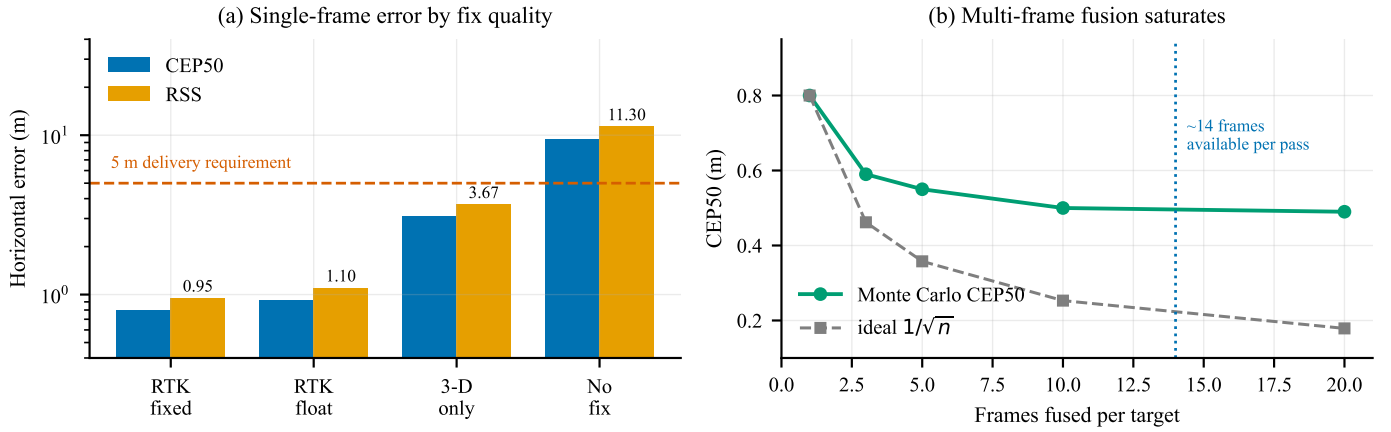


Fig. 3. Geolocation error, from a Monte Carlo run through the same projection code the aircraft flies. (a) Single-frame horizontal error against GNSS fix quality, typical attitude, on a logarithmic scale; the dashed line is the 5 m delivery requirement. (b) Effect of fusing multiple observations of the same target, RTK fixed. Generated by `figures/make_figures.py` from `docs/sizing/geotag-accuracy-output.txt`.

TABLE III
PROGRAMME PHASES

Ph.	Title	Principal exit criterion
P1	Requirements and sizing	Design point frozen; all models regenerate
P2	Ground segment	Single-operator interface demonstrated against three simulated aircraft
P3	Autonomy	Deterministic plan generation; deconfliction verified in simulation
P4	Fault handling	Link-loss and low-battery behaviour verified by fault injection
P5	Procurement and build	Three airframes assembled and weighed; thrust stand complete
P6	First flight	Hover, trim, vibration and thermal characterisation
P7	Perception field trials	Detection recall measured on real imagery against fabricated targets on RTK-surveyed ground
P8	Delivery trials	Delivery CEP measured against a surveyed target mat
P9	Full mission rehearsal	End-to-end mission with all three aircraft, no operator intervention
P10	Setup and contingency	Setup drill timed over repeated runs; margin recovered

constraint on the entire programme, and the work plan is arranged to protect it.

A. Verification strategy

The programme’s verification discipline is, I believe, its most transferable contribution, and it exists because of a specific and recurring class of defect.

On four separate occasions during preparatory work, a configuration artefact was found to be correct, unit-tested, reviewed, and *not in the execution path* of the running system. In one instance a validated failsafe parameter set was never loaded by any simulation, so every test ran against stock

defaults in which the low-battery action was disabled. In another, a message-routing configuration started cleanly and forwarded zero messages for weeks. Each of these reviewed clean and had passing tests around it.

The countermeasure adopted is procedural rather than technical: no capability is considered demonstrated until the real artefact has been exercised end to end and the resulting values read back off the running system. Consequently every claim in this proposal carries an explicit evidence class, and those classes are maintained mechanically rather than editorially:

- **Measured** — observed on a running system, in software or in hardware-in-the-loop simulation.
- **Modelled** — computed by a model whose inputs are themselves assumptions, and which regenerates in continuous integration.
- **Assumed** — neither measured nor modelled; carried explicitly as a risk.

A continuous-integration job enforces the rule that every published number regenerates byte-for-byte from its model, so that changing a model without committing its regenerated output fails the build. Thirteen model outputs are currently under this gate.

VI. PRELIMINARY RESULTS

Substantial work has been completed before this request. I summarise it here with the evidence class of each result stated, because a claim whose basis is declared can be independently checked, whereas a claim whose basis is left implicit cannot be.

A. Measured in simulation

- **Low-battery failsafe returns the aircraft to the pad.** Verified across three simultaneous software-in-the-loop autopilots; return-to-launch triggered at 10 809 mAh of a 10 800 mAh planned consumption.
- **Three aircraft on one ground station.** A single telemetry router carried three distinct system identifiers to one ground station port with all three arriving.

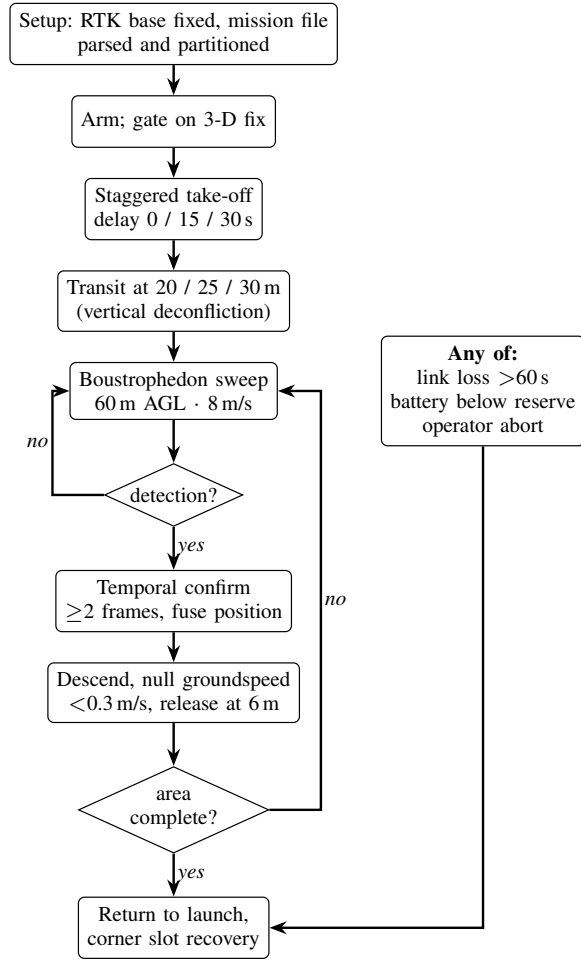


Fig. 4. Autonomous mission sequence. The take-off stagger is encoded in the mission file rather than in operator timing, and all three abnormal conditions converge on a single return-to-launch path.

- **Inter-aircraft separation at launch.** Staggered take-off delays encoded in the mission file, rather than in operator timing, increased the closest airborne approach during launch from 1.31 m to **64.80 m** (Fig. 5). Both figures are recomputed directly from the committed telemetry.
- **Separation during the sweep.** Minimum airborne separation away from the pad is **29.19 m**, with staggered transit altitudes of 20/25/30 m providing vertical deconfliction independent of the lateral plan.
- **Recovery deconfliction.** Assigning landing slots to the corners of the recovery pad rather than in a row increased slot spacing from 1.22 m to 2.61 m at no cost, raising the measured minimum approach from an overlapping 0.83 m to **2.27 m** — a clearance of 1.22 m between airframes (Fig. 6). Separation while stacked in the air over the pad improves by the same mechanism.
- **Ground station.** All eight required operator displays were verified against three simultaneous autopilots, carrying three concurrent H.264 streams within the link budget, with offline map tiles (Fig. 8).

B. Modelled

Endurance, hover power, mass budget, thermal margin, link budget, delivery dispersion and geolocation error are all modelled and regenerate from source. The geolocation Monte Carlo reconciles with the independent analytic budget to within one per cent, and the geotag projection has been verified self-consistent between two independent formulations to 7.8×10^{-10} m.

C. Assumed, or not yet implemented

Detection recall on real post-flood imagery, boresight calibration residual, achieved RTK accuracy in the field, and battery internal resistance under Indian ambient conditions are all assumed. Each requires hardware and is a funded activity in P5–P8.

One ground-segment function is explicitly *not* implemented and is visible as such in Fig. 8: the abort and recall controls currently record operator intent in the mission log but transmit nothing, because no safety radio is yet configured. Recovery today depends on the safety pilot’s transmitter. Closing this is a P4 activity and is gated on the sub-gigahertz link discussed in Section IV-E.

D. The honest summary

Nothing in this programme has flown. Every “measured” result above was measured in simulation or in software. That rules out whole classes of logical and integration error and rules out none of the physical ones. The requested funding exists principally to convert the modelled and assumed rows of this section into measured ones.

VII. BUDGET AND COST ANALYSIS

A. Basis of estimate

The cost basis is arithmetic over a bill of materials in which each line carries an exact manufacturer part number, an Indian supplier, and a source. Lines are classified by price provenance: *listed* where a dated Indian retail price was obtained, and *quote required* where no public price exists. I regard the distinction as material. Four of the six largest lines in the aircraft — the autopilot, the motor, the cells and the camera — have no public price and require supplier quotation, and the cost basis carries that uncertainty explicitly rather than concealing it in a rounded figure.

B. The bill of materials in detail

Table IV gives the air-vehicle bill of materials at subsystem granularity, with the indigenous fraction each subsystem carries. The full line-level sheet holds 41 entries, each with a manufacturer part number, an Indian supplier and a source link; it is summarised here rather than reproduced.

Two subsystems dominate and they pull in opposite directions. Avionics is the largest line and is also comparatively indigenous, because a Pixhawk-standard autopilot is manufactured domestically. Compute and perception is the second largest and the least indigenous, at 33 %, for the single reason developed in Section VIII: no Indian accelerator exists in this class.

Launch sequencing — NAV_DELAY 0/15/30 s before each takeoff

Recorded from three ArduCopter SITL. Left: every aircraft leaves the pad at once. Right: the mission file staggers them. First 60 simulated seconds.


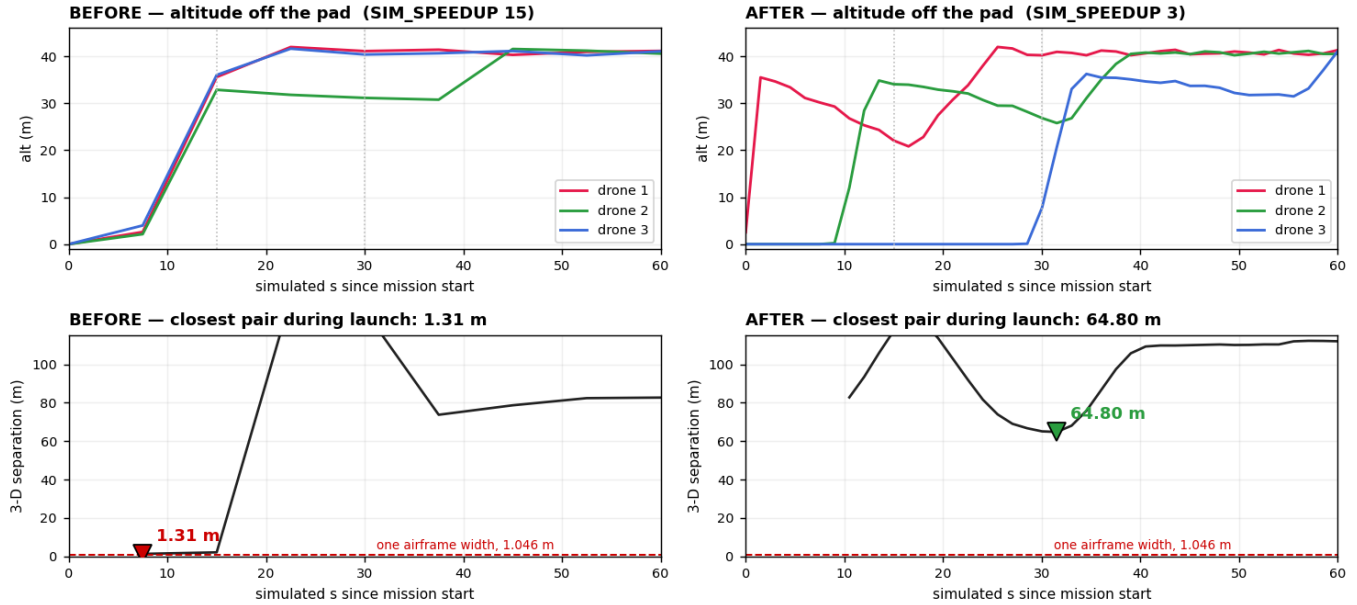


Fig. 5. Launch deconfliction, recorded from three ArduCopter software-in-the-loop autopilots. Left: all three aircraft leave the pad together and the closest pair passes within 1.31 m — inside one airframe width. Right: a delay encoded in the mission file before each take-off command staggers them, and the closest airborne pair is 64.80 m. Both figures are reproducible from the committed telemetry.

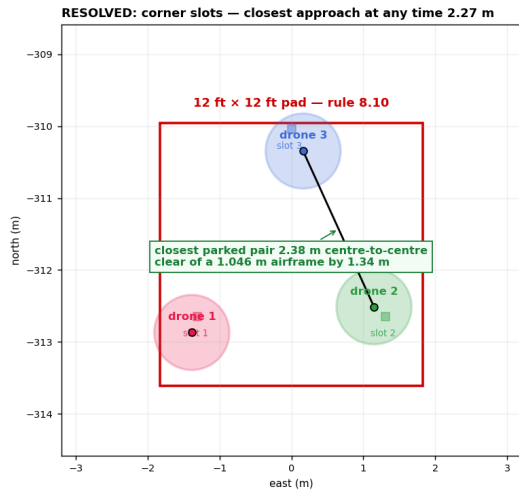

A ROW of three gave 1.22 m spacing and they landed 0.83 m apart — an overlap of 1.046 m airframes. Centres must stay half an airframe inside the pad edge, so they live in a 2.61 m square; its CORNERS are 2.61 m apart — two Worst case with ± 0.5 m touchdown dispersion on each aircraft: 1.61 m, still clear. Holding over points 2.6 m apart instead of the stacked-over-the-pad separation from 3.99 m to 6.52 m.

Fig. 6. Recovery deconfliction on the landing pad. Slot centres must remain half an airframe inside the pad edge, so they occupy a 2.61 m square; a row across that square gives 1.22 m of spacing, its corners give the full 2.61 m. The measured closest approach at any time rises from an overlapping 0.83 m to 2.27 m — twice the separation, same pad, no cost.

TABLE IV
AIR VEHICLE BOM BY SUBSYSTEM, OPTION A (PER AIRCRAFT)


Subsystem	INR	Ind. Governing driver
Avionics	85 400	60 % Autopilot, RTK pair
Compute, perception	79 500	33 % Inference throughput
Propulsion	57 396	89 % Thrust at MTOW
Power	24 500	58 % 292 Wh reserve
Structure	20 550	79 % Arm root moment
Communications	17 800	42 % Three-feed budget
Payload system	5 400	61 % Four stations
Total	290 546	58 %

C. Cost reduction study

A structured cost-reduction study was performed against the verified bill of materials, producing four costed configurations of the same aircraft plus one reduced-capability alternative. Table V and Fig. 9 summarise them; Fig. 10 shows, for the intermediate step, where a saving of this kind is actually taken.

The options are ordered by *what they trade*, not by descending price, because the interesting question is not how cheap the aircraft can be made but what each rupee costs in capability or sovereignty.

Option D is adopted, at INR 157 800 per aircraft. The governing principle is not "buy cheaper" but *hobby-grade where the failure mode is visible and the specification is easy*

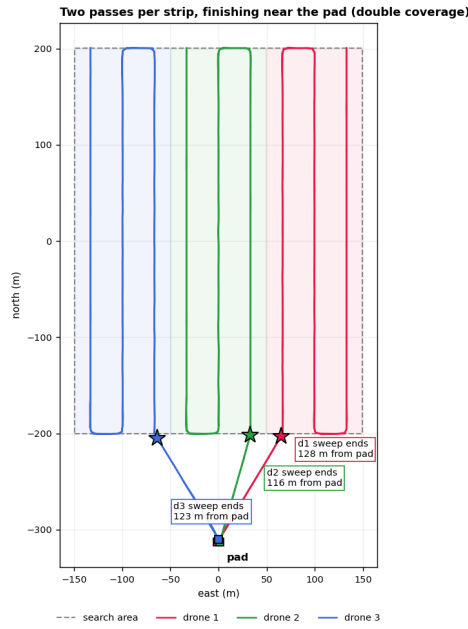

Each strip is swept TWICE — the second pass retraces the same ground on the reverse heading, so the two overlap here. The evident 18/19/19 items against 12/13/13 for a single pass, and 2535 m of path against 1267 m. It is for the GEOTAG, not coverage: boresight systematic, and only cancels when the same ground is seen from the opposite direction. The cost is a second sweep, 347 s against 1 Sweep also finish near the pad now — 116-123 m, against 516 m and 540 m for two of three aircraft before.

Fig. 7. Coverage decomposition and return geometry. Each aircraft is assigned an equal-area strip and flies a boustrophedon pattern within it. Enumerating the four start-side and direction combinations and keeping the one that ends nearest home brings all three aircraft back within 116–128 m of the pad, against 516 m and 540 m for two of three aircraft under the previous indexed rule — at identical path length.

TABLE V
COSTED CONFIGURATION OPTIONS (PER AIRCRAFT)

Opt.	What it trades	INR	Indian	Cost
A	Verified baseline	2 90 546	58 %	—
B	Efficiency only	2 63 401	61 %	nothing
C	+ indigenisation	2 37 081	53 %	Indian content
D	ADOPTED	1 57 800	45 %	margin, not capability
E	Different aircraft	37 309	—	the mission

to verify; professional where it is not.

Motors, electronic speed controllers, propellers, adapters, pack hardware, the mesh node and mounts are commodity parts whose ratings can be checked on a bench before they fly. Six lines are held at professional grade on purpose, and the reason is recorded against each: the autopilot (dual IMU, Pixhawk standard), the RTK receiver (no cheaper part exists, and it governs 125 of 200 geolocation points), the accelerator (26 TOPS is the specification floor rather than a preference), the camera (ground sample distance drives detection), the cells (capacity- and IR-matched, because one weak cell defines the whole pack), and the airframe structure.

This is bought with margin, not with capability. Every scored function survives: RTK geolocation, onboard detection at rate, three concurrent video feeds, four-station delivery.

What is given up is reserve — published thrust data, supplier support, spares depth and indigenous content.

The accelerator substitution carries an integration consequence I did not see at first and record here because it enlarges the benchmark rather than the bill. The displaced module has a *hardware* H.264 encoder; the single-board computer that replaces it has none — its GPU dropped every encode block, so all video encoding is done in software on the same CPU that feeds the accelerator. Each aircraft encodes only its own stream, so this is one 720p encode per board and is achievable, but it is not free. **The P5 benchmark is therefore not merely whether the accelerator reaches 24 inferences per second; it is whether the board sustains that rate and a 720p H.264 encode simultaneously without thermal throttling.** The cooling line has been left untouched for the same reason.

The generic motors move an existing risk rather than creating one. The selected parts carry no published thrust curve, where the displaced ones did. That does not change the physics — it changes who measures it. The thrust stand in Table VI is therefore no longer a convenience: it is the instrument that determines whether the aircraft hovers at the design point, and it is scheduled before design freeze rather than after.

1) *Corrections made to this analysis on review:* A first pass at this study reported a floor of INR 1 29 632 and attributed a 125-point geolocation penalty to Option C. Both were wrong, and the errors are recorded here rather than quietly fixed, because a reviewer who cannot see the corrections cannot judge the method.

Option C does not lose RTK, and its geolocation penalty is negligible. The saving in question deletes the second GNSS receiver, which supplies moving-baseline heading. Substituting the magnetometer-class attitude allocation of Table II into the case-C budget moves the total from 1.304 m to 1.322 m — an 18 mm degradation, not a scoring event. The 125-point penalty belongs to Option D, which deletes RTK itself.

Three savings were withdrawn as unsound. A motor substitution booked INR 8 396 at a price below the lowest listing found for any comparable part, which is circular given that the same study argues the carried price is optimistic. An ESC substitution booked INR 1 600 against a part whose catalogue advertises 30–45 A for a 60 A requirement, which is not a substitution but a specification failure. A sub-gigahertz radio was priced at INR 1 560 in the lowest option while the same document argued that figure does not buy a compliant 865–867 MHz link. Compliance is not an option-level choice, so the compliant price is now carried in every column.

The floor moved upward by INR 54 008 as a result — from INR 1 29 632 to INR 1 83 640. The conclusion this strengthens rather than weakens: an aircraft that flies this mission cannot be built for INR 1 00 000, and the corrected figure is further from that target than the first estimate was.

2) *Why the second GNSS receiver is deferred to a measurement:* Given that its budgeted contribution is 18 mm, the honest case for the second receiver was never the error budget — it is insurance against a risk the budget does not model.

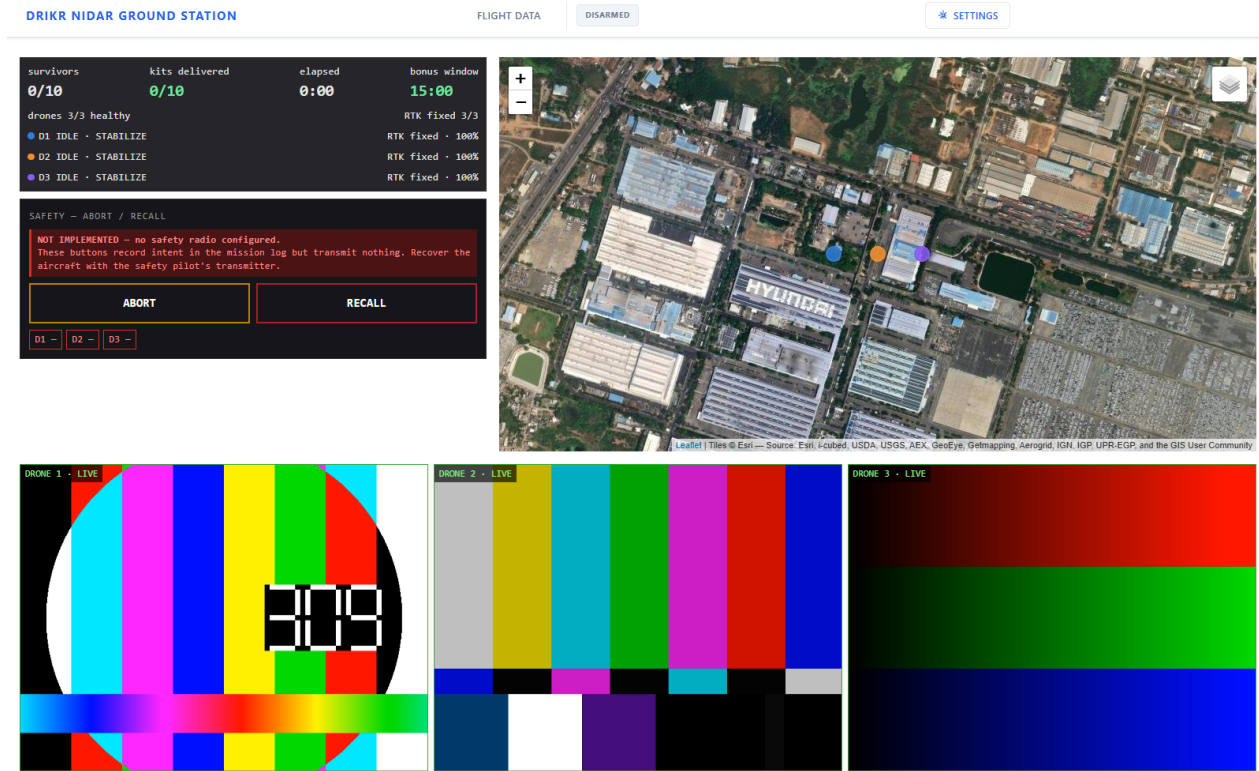


Fig. 8. Ground control station carrying three concurrent H.264 streams within the link budget, with offline map tiles and per-aircraft status. Note the safety panel: abort and recall currently record operator intent in the mission log but transmit nothing, because no safety radio is yet configured. This is reported here rather than cropped out — see Section VI-C.

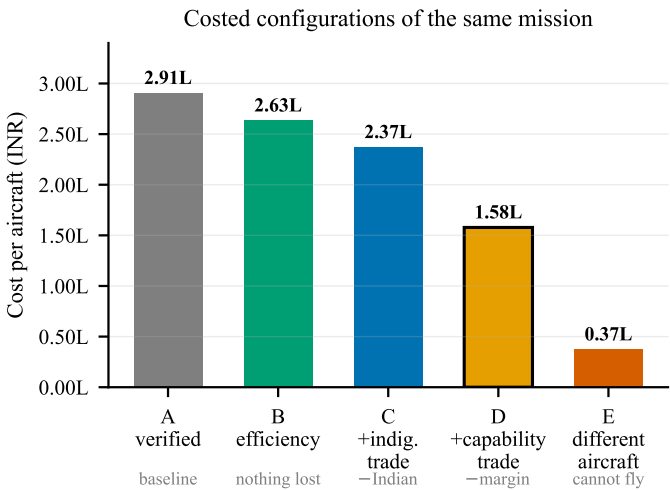


Fig. 9. Costed configurations, ordered by what each trades away. A through D are the same aircraft; E is a different and much smaller airframe that cannot carry the payload, included to show where the cost floor genuinely lies rather than as a proposal. Option D is adopted: it gives up margin and indigenous content, but no scored capability.

The budget allocates a small attitude term on the assumption of good heading. A magnetometer mounted near a 98 A power bus may not deliver that: at the frame edge, 37 m off nadir, a heading error of 5° displaces a detection by 3.22 m, which

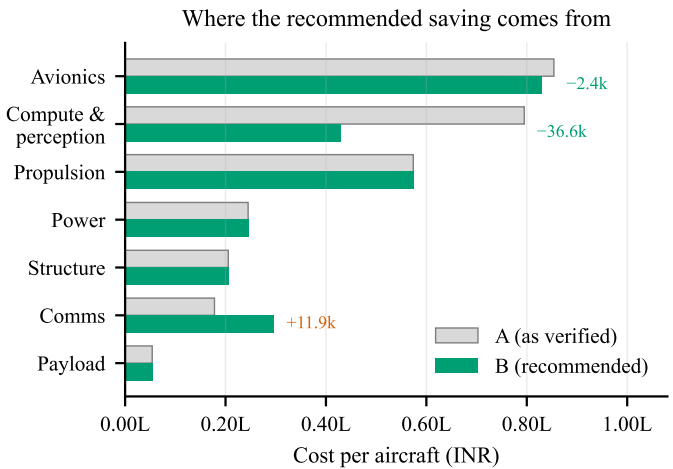


Fig. 10. Subsystem cost, Option A against the intermediate Option B, shown because it isolates one effect cleanly: almost the whole saving at that step is a single substitution in compute and perception. Communications moves the other way, the sub-gigahertz link being corrected *upward* before it was later deferred entirely.

would consume the entire delivery allowance on its own.

That is a real risk, but it is an *unmeasured* one, and INR 51 000 is a great deal to pay to avoid a measurement the programme will make regardless. **P6 characterises achieved heading accuracy on the built aircraft at no additional**

TABLE VI
COMPETITION BUILD COST

Element	Was	Ask
Air vehicles (3) and payload	8.31 L	4.83 L
Ground segment	3.88 L	0.74 L
Test equipment	2.26 L	0.36 L
Spares and consumables	2.73 L	0.59 L
Regulatory	1.75 L	0.05 L
Subtotal	18.93 L	6.53 L
Duty and freight, imported residual		0.79 L
Goods and services tax		1.32 L
Contingency, 15 %		1.30 L
Total requested		9.94 L

cost. If it exceeds roughly 1° the receiver is reinstated and the money is well spent; if it does not, it was never needed. Deferring on evidence rather than on funding is the distinction the reinstatement table in Section VII-E draws, and this is the line that motivated it.

Options A to C are retained in Table V as the reasoning that led to D, not as live alternatives: each is a step in the argument, and a reviewer should be able to see the sequence rather than only its conclusion. Option E is a reduced training platform that cannot carry the payload at all and is discussed in Section VII-G.

D. What is actually being requested

An earlier version of this budget costed a development programme at INR 28.74 L. That figure bought laboratory equipment, computing and a purchased field-data campaign. On review, none of those are what a competition entry needs, and most of the equipment is already held by the host institution. The ask has been recosted accordingly and is now **INR 9.94 L**, a reduction of 65 %. Table VI gives the breakdown.

E. What is deferred, and what it would cost to reinstate

The ask above is the minimum that flies the scored mission. Several items were deliberately deferred rather than judged unnecessary, and Table VII lists them in the order I would reinstate them against additional funding. Stating them is not padding: a reviewer should be able to see what the lowest-cost configuration gives up.

Ground-truth apparatus is fabricated rather than bought, taking that line from INR 35 280 to INR 4 860. Survivor targets are clothed forms of the correct size and outline; at 60 m and 2 cm/px a person subtends about fifty pixels, and what the detector responds to is silhouette, scale and contrast against terrain, not anatomy. Two of these items are *better* fabricated: dummy kits can be made to exactly the 200 g that rule C6 fixes, and donated clothing gives wider colour and contrast variety than matched bought sets, which is precisely what detection robustness requires.

One caveat follows from this and is recorded rather than glossed. The calibration markers are surveyed using

TABLE VII
DEFERRED ITEMS, IN REINSTATEMENT PRIORITY

#	Item	INR	What it buys back
1	Flight insurance	25 000	Must be confirmed — see below
2	Second GNSS receiver (3)	51 000	Conditional on a measurement , not on funding
3	Recovery parachutes (3)	36 000	~40 points per crash avoided
4	Training airframe	37 309	Protects the fleet in week 1
5	Sub-GHz safety radio (3)	58 065	A third independent link
6	Spare packs and motors	74 396	Survives a crash mid-campaign
7	Field data campaign	15 000	Detection recall measured, not modelled
8	Spare compute module	20 000	Removes a single point of failure
Total deferred		3.17 L	

the programme's own RTK rover. That is standard practice and adequate for this purpose, but it means the ground truth against which geolocation accuracy is measured is *itself RTK-derived*. The two error sources are therefore correlated, and the measured geotag figure reported in P7–P8 will be slightly optimistic against an independently surveyed datum. Any accuracy claim arising from those phases will state this.

Four further items deserve comment rather than a table row.

The second GNSS receiver is deferred to a measurement, not to funding. It supplies moving-baseline heading, and Section IV-C shows that substituting a magnetometer-class attitude allocation into the case-C budget costs **18 mm**. The honest case for it was never the error budget — it was insurance against a magnetometer sitting near a 98 A bus, which the budget does not model. That is an unmeasured risk, and INR 51 000 is a great deal to pay to avoid a measurement I intend to make anyway. **P6 characterises achieved heading accuracy on the built aircraft; if it exceeds roughly 1° , the receiver is reinstated** and the money is well spent. If it does not, it was never needed.

The sub-gigahertz safety link is deferred on an architectural argument. The ExpressLRS link at 2.4 GHz carries safety-pilot control and abort independently of the autonomy stack, and the mesh at 5.8 GHz carries video, telemetry and coordination. Those are already two independent bands across a 600 m geofence, and the ExpressLRS link covers that range with substantial margin. The 865–867 MHz set is a *third* path. It is the correct thing to add when funding allows, and it is not the thing to buy before the aircraft flies.

Insurance is deferred at the team's direction and I flag it as the one item that may not be optional. Third-party cover

is commonly mandatory for unmanned operations in India. It must be confirmed against the rulebook and the prevailing DGCA rules **before any flight**, and if it is required it ceases to be a budget decision.

The recovery parachute is permitted, not required. An earlier draft of this proposal stated that a requirement mandated it; that was wrong. The organisers permit ballistic recovery, and the case for fitting one is a points argument rather than a compliance one — a crash is scored at -50 against -10 for landing outside the recovery zone, so deployment is worth roughly 40 points before the value of the airframe is counted. Deferring it is an accepted risk, taken knowingly.

No spectrum licence is required and none is budgeted. Every link in the system operates in a delicensed band: 2.4 GHz and 5.8 GHz ISM for the mesh and control links, and 865–867 MHz for the independent safety link. Equipment type approval is a supplier obligation, discharged by purchasing approved radios from Indian vendors, so only DGCA aircraft registration remains as a regulatory line.

Four principles were applied, and each is visible in the table.

If the institution already owns it, it is not in the ask. **INR 3.54 L of equipment** is available and has been removed: the electronics laboratory and 3D printing (INR 84 000), GPU compute for model training (INR 75 000), field power (INR 55 000), and the machine shop and composite fabrication that produce the CNC-cut plates, machined arm clamps and motor mounts. Both ground-station laptops (INR 1,40,000) are supplied by the team. None of this is deleted — it is recorded as an **institutional contribution**, because that is what it is: co-funding in kind, and the reason the ground segment falls from INR 3.88 L to INR 1.37 L.

The remaining ground-segment spend is dominated by one item that could *not* be borrowed: the RTK base receiver and its survey tripod (INR 47 500). Section IV-C explains why it is not a candidate for deletion — it governs the entire geolocation budget.

If it can be built, it is costed as built. The thrust stand falls from INR 45 000 to INR 8 000 — a load cell, an amplifier and a printed fixture. Motor thrust verification is a flagged risk in Table X; building and calibrating the instrument is a better answer to that risk than a purchase order for one.

Spare cover what crashes, not what fails rarely. Propellers, motors, arms, plate stock and packs are retained. Spare autopilot, GNSS and camera — INR 60 600 together — are removed. **This is an accepted risk and I state it as one:** a failure of any of those three during the flight-test window costs schedule, and the mitigation is procurement lead time rather than inventory.

What is deferred is listed, not hidden. Section VII-E sets out every item removed to reach this figure, in the order I would reinstate it against additional funding. The lowest-cost configuration is a deliberate choice, and a reviewer should be able to see exactly what it gives up.

The contingency is held at 15 % rather than 20 %, which the phased disbursement in Section VII-F makes defensible: unreleased tranches are themselves a reserve, and holding both is asking for the same margin twice.

TABLE VIII
PHASED DISBURSEMENT SCHEDULE

T	Months / phases		INR	Release condition
1	1–2	P1–P4	3.50 L	On award. Design point frozen; models regenerate
2	3–4	P5	2.95 L	Ground segment demonstrated against three simulated aircraft
3	5–6	P6–P8	2.10 L	Three airframes weighed; first hover complete
4	7–8	P9–P10	1.39 L	Perception and delivery trials reported with measured figures
Total			9.94 L	

F. Phased disbursement

The full sum is not required at once. The programme is structured as four tranches tied to the phase exit criteria of Table III, and I would rather be funded against demonstrated progress than hold a sponsor’s capital for eight months. Table VIII and Fig. 11 give the schedule.

Three properties of this schedule are deliberate.

Tranche 1 is front-loaded and mostly procurement. The largest single schedule risk in the programme is that long-lead components arrive late and compress the flight-test window. Cells, autopilots and GNSS receivers are ordered in month one, before most of the software work is finished, because the lead time is the constraint rather than the readiness of the integration.

Each tranche is released against a stated, checkable exit criterion drawn from Table III — not against a date and not against a progress report. A sponsor can verify every one of them from the artefacts the programme already produces.

Tranche 4 is the smallest and holds the contingency. If the programme underperforms, the unreleased balance is the sponsor’s, and the exposure at any point is bounded by the cumulative curve in Fig. 11 rather than by the total.

G. A note on the training platform

Option E in Table V is a INR 37 309 training airframe. It fails eight system requirements and cannot fly the mission; it is emphatically not a low-cost variant of the proposed system. Its value is different: the programme’s binding constraint is an eight-week flight-test window currently budgeted entirely on aircraft that do not yet exist and cannot be risked once they do. A training airframe, at roughly twice the cost of one inference module, would fly from the first week of that window and absorb ground-station integration, radio-path validation, setup-drill timing, failsafe verification on real hardware, and crash-and-rebuild practice.

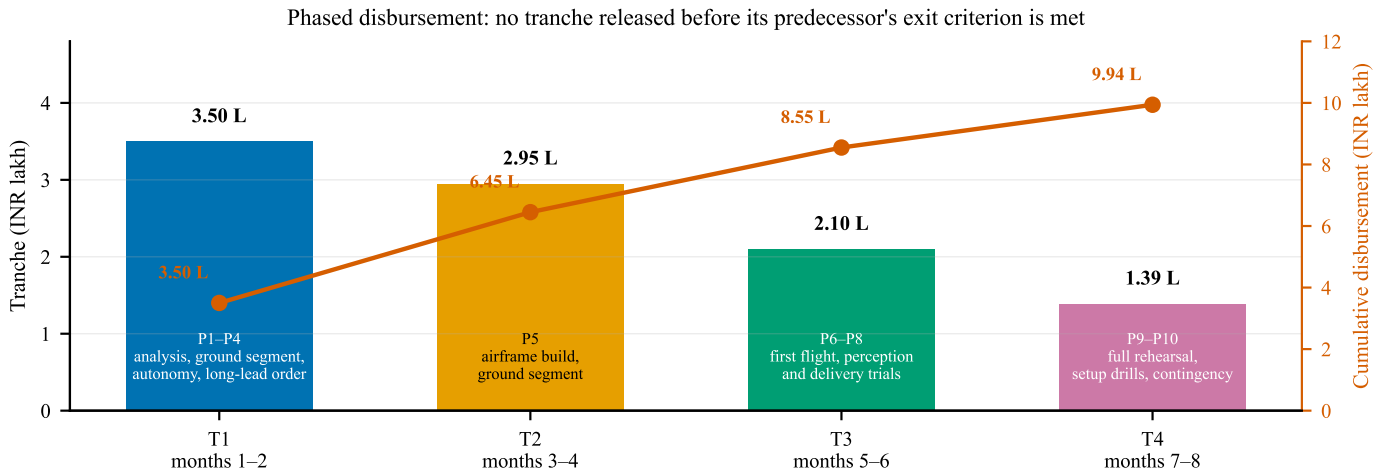


Fig. 11. Phased disbursement against programme phases. Tranche 1 is front-loaded because long-lead components must be ordered in month one for the eight-week flight-test window to survive; tranche 4 is the smallest and carries the contingency.

extbflt is deferred in the present ask and sits at position 4 in Table eftab:deferred. I record it as the highest return-on-investment discretionary item in the budget rather than quietly dropping it: with the spares set also reduced, it is the mitigation the flight-test window most obviously lacks.

VIII. INDIGENISATION STRATEGY

Indigenous content is measured, not asserted. Every line in the bill of materials carries a declared Indian value fraction, and the aggregate is computed rather than estimated, which makes the claim auditable.

The configuration adopted in Section VII-D carries approximately 45 % Indian content, down from 58 % in the fully specified aircraft. I report the figure that applies to what is actually being funded rather than the one that flatters the argument, and the fall is a direct consequence of the cost reduction: the imported autopilot and generic propulsion are what make the aircraft affordable, and they are also what make it less Indian.

Fig. 12 decomposes the fully specified aircraft, and the decomposition remains the more informative view. Indigenous content is not spread evenly: it is high where Indian industry is genuinely strong (propulsion at 89 %, composite structure at 79 %) and low in exactly one place.

This is the clearest cost of the budget decision, and it is reversible. Two lines account for almost all of it — the Indian autopilot (INR 19 400 per aircraft) and Indian propulsion (INR 18 396 per aircraft). Both are drop-in reinstatements requiring no redesign. Component sponsorship from the Indian suppliers surveyed for this bill of materials is the intended route, and it is the reason those suppliers are named throughout rather than described generically.

The inference accelerator is the one genuinely irreducible import, and I declare it plainly rather than obscuring it. Mitigation is confined to what is honest: an Indian carrier board, and Indian enclosure and thermal design. I regard an explicit gap analysis as more credible than a uniformly confident claim,

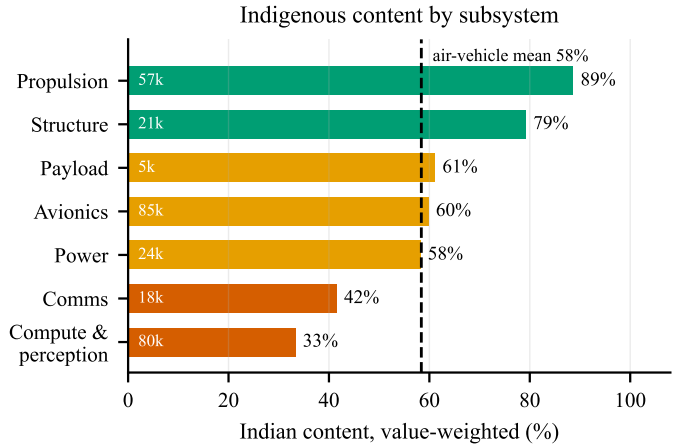


Fig. 12. Indian content by subsystem, value-weighted, with subsystem cost annotated inside each bar. The single subsystem below 40 % is also the second most expensive, which is what makes the aggregate figure worth decomposing rather than quoting alone.

and I note that the domestic RISC-V development kit carried on the aircraft is a genuine demonstration of Indian silicon in flight, albeit in a monitoring role rather than as an accelerator.

IX. RISK REGISTER

I draw particular attention to the setup-time risk. It is currently supported by a model with a modest margin and no measurement, and it gates the entire mission. Timed bench drills are scheduled as the earliest hardware activity in the programme for precisely this reason.

X. EXPECTED OUTCOMES AND DELIVERABLES

- 1) Three flight-qualified aircraft with a documented, market-verified bill of materials at approximately 45 % Indian content, and a costed route to restoring the deferred Indian autopilot and propulsion.

TABLE IX
INDIGENISATION STATUS BY SUBSYSTEM

Subsystem	Status
Autopilot	<i>Deferred:</i> Indian Pixhawk-standard board, domestically made
Propulsion	<i>Deferred:</i> Indian motors and ESCs with published thrust data
Airframe	Indian composite fabrication
Cells	Indian, BIS-certified 21700 NMC
Camera	<i>Deferred:</i> Indian embedded-vision supplier
GNSS	Indian receiver, NavIC L1+L5.
Co-processor	<i>Retained</i> Indian RISC-V development kit
Inference module	No Indian equivalent exists at this class

- 2) A single-operator ground control station demonstrated end to end against real aircraft, with no network dependency.
- 3) A measured detection recall figure against fabricated survivor targets on surveyed ground, replacing the current assumption. Ground truth is RTK-derived rather than independently surveyed, and the resulting figure will state that.
- 4) A measured delivery circular error probable against a surveyed target, replacing the current model.
- 5) A measured setup-to-launch time distribution over repeated drills.
- 6) An open, reproducible evidence base in which every published figure regenerates from its model under continuous integration.
- 7) A supply-chain report identifying, for each subsystem, the domestic capability that exists, the capability that does not, and what would be required to close the gap.

The seventh deliverable may prove the most durable. The exercise of sourcing a complete airframe domestically, at component granularity and with verified prices, produced a map of Indian UAV supply-chain maturity that I have not seen published elsewhere, including the specific and narrow point at which it currently fails.

XI. FUTURE WORK

This proposal deliberately asks for a competition build and nothing more. The work has a longer arc, and I set it out here so that the scope of the present request is unambiguous by contrast.

A. From a competition entry to a deployable system

The entry is not a product. Reaching one requires, in rough order: night and all-weather capability through thermal imaging, which is the single highest-value sensing extension and is excluded here only because it doubles the perception budget; beyond-visual-line-of-sight approval, which is a regulatory programme rather than an engineering one; ingress

TABLE X
PRINCIPAL RISKS AND MITIGATIONS

Risk	Sev.	Mitigation
Detection recall below target on real imagery	High	Raised by deferral of the field data campaign. Public aerial-person datasets carry the model; tiling and fusion parameters remain tunable without hardware change
Inference and software video encode contend on one board	High	The replacement compute has no hardware H.264 encoder. Benchmark both loads together before design freeze; fallback is a reduced tile count on a centre crop
RTK capability unconfirmed on selected receiver	High	Supplier confirmation is a gating procurement action; degraded mode already specified and flagged to the operator
Flight-test window compressed by procurement delay	High	Raised by deferral of the training airframe and of spares. Lead time is now the only mitigation, so long-lead items are ordered in tranche 1
Recovery parachute sizing and supply	Medium	No domestic supplier identified; import lead time and correct mass rating are open procurement actions
Setup time exceeds allowance	Medium	Currently modelled, not measured; timed drills are the highest-priority early test
Motor thrust below the datasheet claim	High	Selected motors publish no thrust curve. The thrust stand is built in P5 and characterises them before design freeze
Airframe loss during test	High	Raised by deferral of spares. Structure set and consumables retained; a second loss in the same week is uncovered
Flight insurance may be mandatory	Medium	Deferred at team direction. To be confirmed against the rulebook and DGCA rules before any flight

protection and thermal qualification for monsoon conditions; and endurance beyond the present 15.3 minutes, which at this payload means a different airframe class rather than a better battery.

B. Cost at production volume

Every figure in Section VII is single-unit retail for a build of three. The marginal cost of an additional aircraft is already

substantially below the per-aircraft figure quoted here, because the ground segment, test equipment and spares are one-off. At production volume the relevant questions are different ones — tooling amortisation, negotiated component pricing, and assembly labour — and none of them can be answered honestly from a three-aircraft bill of materials. I decline to extrapolate them.

C. A route to commercialisation

The natural customers are state disaster management authorities and the national and state disaster response forces. Establishing whether that is a viable business requires three things this programme does not attempt: the size and refresh rate of the addressable fleet, what a comparable capability is currently procured for, and the operating cost per flight hour of the boat or helicopter search it would displace. Those are questions for published tender data and operator interviews, not for a bill of materials, and I would rather name them as open than fill them with plausible figures.

What this programme does produce toward that end is the seventh deliverable in Section X: a component-level map of where Indian UAV supply chain capability exists and where it does not. That artefact outlives the competition regardless of what follows it.

XII. CONCLUSION

I propose an autonomous three-aircraft system that addresses the localisation bottleneck in post-flood search and rescue, sourced domestically wherever the requested budget permits, and engineered under a verification discipline that distinguishes what has been demonstrated from what has merely been designed. Where an Indian part was deferred it was deferred on cost, not on capability — domestic industry can supply the autopilot and the propulsion, and Section e-se:indig states what restoring them costs.

The system's design point, error budgets and cost basis are established and reproducible. Its coordination and failsafe behaviour have been demonstrated in hardware-in-the-loop simulation across three simultaneous autopilots. What remains is the part that requires funding: to build the aircraft, fly them, and replace the modelled and assumed quantities in Section V-A with measured ones.

I am asking for INR 9.94 L to do that, and I have tried throughout this document to make every number in it checkable.

ACKNOWLEDGMENT

I thank the Department of Electronics and Communication Engineering, Thapar Institute of Engineering and Technology, for institutional support.

REFERENCES

- [1] A. C. Kapoutsis, S. A. Chatzichristofis, and E. B. Kosmatopoulos, "DARP: Divide areas algorithm for optimal multi-robot coverage path planning," *Journal of Intelligent & Robotic Systems*, vol. 86, pp. 663–680, 2017.
- [2] H. Choset, "Coverage of known spaces: the boustrophedon cellular decomposition," *Autonomous Robots*, vol. 9, no. 3, pp. 247–253, 2000.
- [3] H.-L. Choi, L. Brunet, and J. P. How, "Consensus-based decentralized auctions for robust task allocation," *IEEE Transactions on Robotics*, vol. 25, no. 4, pp. 912–926, 2009.
- [4] F. C. Akyon, S. O. Altinuc, and A. Temizel, "Slicing aided hyper inference and fine-tuning for small object detection," in *Proc. IEEE International Conference on Image Processing (ICIP)*, 2022, pp. 966–970.
- [5] S. Sambolek and M. Ivasic-Kos, "Automatic person detection in search and rescue operations using deep CNN detectors," *IEEE Access*, vol. 9, pp. 37 905–37 922, 2021.
- [6] P. Zhu *et al.*, "Detection and tracking meet drones challenge," *IEEE Transactions on Pattern Analysis and Machine Intelligence*, vol. 44, no. 11, pp. 7380–7399, 2021.
- [7] S. G. Mathisen, F. S. Leira, H. H. Helgesen, K. Gryte, and T. A. Johansen, "Autonomous ballistic airdrop of objects from a small fixed-wing unmanned aerial vehicle," *Autonomous Robots*, vol. 44, pp. 859–875, 2020.
- [8] Internal Displacement Monitoring Centre, *Global Report on Internal Displacement 2025*, Geneva, 2025. [Online]. Available: <https://www.internal-displacement.org/countries/india/>
- [9] ArduPilot Development Team, "ArduPilot: open source autopilot software suite," 2026. [Online]. Available: <https://ardupilot.org/>
- [10] T. Takasu and A. Yasuda, "Development of the low-cost RTK-GPS receiver with an open source program package RTKLIB," in *Proc. International Symposium on GPS/GNSS*, 2009.
